


Designate location of all lateral arms and longitudinal stabilizing devices on the blocking plan.

Blocking Plan



typical single wide blocking plan

Manufacturer _____
Length x width _____

Lateral Arm



Longitudinal Stabilizing Devices

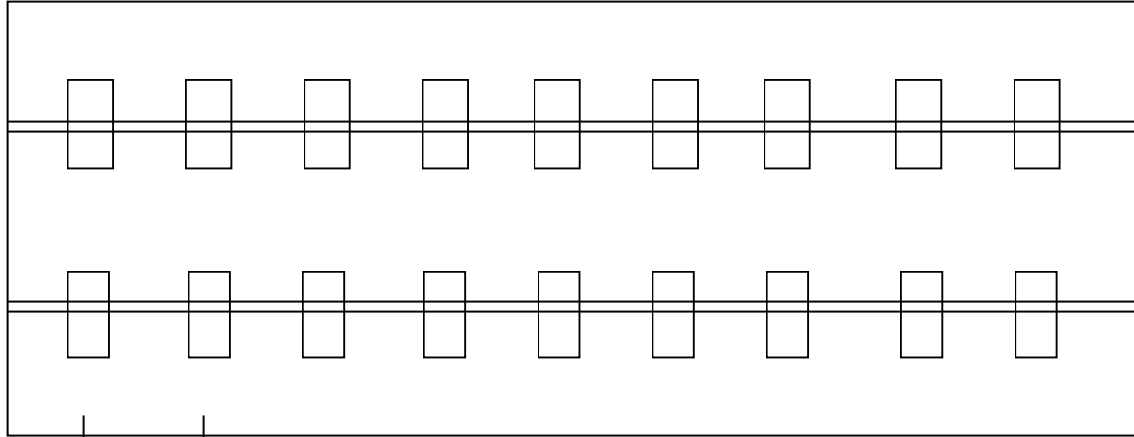

Pocket Penetrometer Test

**Test the perimeter of the home at 6 locations.
Take the reading at the depth of the footer.
Using 500lb increments, take the lowest reading and round down to that increment.**

Pocket Penetrometer test results _____
Soil torque probe test results _____
Anchor Length _____
I-beam pier pad size _____
Perimeter pier pad size _____

Other information
